


# Fedora 14 Documentation & Translation Tasks & Milestones

Name	Start	End	Duration	2010											
				May	Jun	Jul	Aug	Sep	Oct	Nov	D				
Fedora 14	Wed 2010-May-26	Mon 2010-Nov-15	173.8	[Gantt bar from May 26 to Nov 15]											
Planning Phase	Wed 2010-May-26	Tue 2010-Jul-27	62.7	[Gantt bar from May 26 to Jul 27]											
Start Feature Submission	Wed 2010-May-26	Wed 2010-May-26	0	[Milestone diamond at May 26]											
RHT Eng-Ops Fedora 11 EOL auto closure	Fri 2010-Jun-25	Fri 2010-Jun-25	0	[Milestone diamond at Jun 25]											
Testing Phase	Wed 2010-May-26	Mon 2010-Oct-11	138.8	[Gantt bar from May 26 to Oct 11]											
Alpha Release	Wed 2010-May-26	Tue 2010-Sep-21	118.7	[Gantt bar from May 26 to Sep 21]											
Feature Submission Deadline	Tue 2010-Jul-13	Tue 2010-Jul-13	0	[Milestone diamond at Jul 13]											
Custom Spins Submission Deadline	Tue 2010-Jul-13	Tue 2010-Jul-13	0	[Milestone diamond at Jul 13]											
Feature Freeze (Testable Complete)	Tue 2010-Jul-27	Tue 2010-Jul-27	0	[Milestone diamond at Jul 27]											
Spins Freeze--All Fedora 14 Spins Identified	Tue 2010-Jul-27	Tue 2010-Jul-27	0	[Milestone diamond at Jul 27]											
Branch Fedora 14 from Rawhide	Tue 2010-Jul-27	Tue 2010-Jul-27	0	[Milestone diamond at Jul 27]											
Remind f-dev-announce to Rebuild All Translated Packages	Mon 2010-Aug-02	Mon 2010-Aug-02	0	[Milestone diamond at Aug 02]											
Alpha Change Deadline	Tue 2010-Aug-03	Tue 2010-Aug-03	0	[Milestone diamond at Aug 03]											
Software String Freeze	Tue 2010-Aug-03	Tue 2010-Aug-03	0	[Milestone diamond at Aug 03]											
Software Translation	Tue 2010-Aug-03	Tue 2010-Sep-07	35	[Gantt bar from Aug 03 to Sep 07]											
Software Translation Period	Tue 2010-Aug-03	Tue 2010-Sep-07	35	[Gantt bar from Aug 03 to Sep 07]											
Build F-14 collection packages for all language translators	Wed 2010-Aug-18	Fri 2010-Aug-20	2	[Task bar from Aug 18 to Aug 20]											
Review and correct software translation in built UI	Mon 2010-Aug-23	Tue 2010-Aug-31	8	[Task bar from Aug 23 to Aug 31]											
Remind f-dev-announce to Rebuild All Translated Packages	Tue 2010-Aug-31	Tue 2010-Aug-31	0	[Milestone diamond at Aug 31]											
Software: Translation Deadline (PO Files complete)	Tue 2010-Aug-31	Tue 2010-Aug-31	0	[Milestone diamond at Aug 31]											
Software: Start Rebuild all translated packages	Tue 2010-Aug-31	Tue 2010-Aug-31	0	[Milestone diamond at Aug 31]											
Software: Rebuild all translated packages	Tue 2010-Aug-31	Tue 2010-Sep-07	7	[Task bar from Aug 31 to Sep 07]											
Alpha Release Notes	Tue 2010-Aug-10	Mon 2010-Aug-16	6	[Task bar from Aug 10 to Aug 16]											
Start Alpha Beat and Feature Page Review	Tue 2010-Aug-10	Tue 2010-Aug-10	0	[Milestone diamond at Aug 10]											
Comb Beats and Feature Pages for Alpha	Tue 2010-Aug-10	Thu 2010-Aug-12	2	[Task bar from Aug 10 to Aug 12]											
Prepare Alpha Release Notes (1 page)	Thu 2010-Aug-12	Fri 2010-Aug-13	1	[Task bar from Aug 12 to Aug 13]											
Post Alpha Release Notes One-Page	Mon 2010-Aug-16	Mon 2010-Aug-16	0	[Milestone diamond at Aug 16]											
Fedora 14 Alpha Release Readiness Meeting	Thu 2010-Aug-12	Thu 2010-Aug-12	0	[Milestone diamond at Aug 12]											
Create Alpha Announcement (Marketing & Docs)	Thu 2010-Aug-12	Mon 2010-Aug-16	4	[Task bar from Aug 12 to Aug 16]											
Alpha Public Availability	Tue 2010-Aug-17	Tue 2010-Aug-17	0	[Milestone diamond at Aug 17]											

▬ Container Task   
 ▬ Planned Task   
 ▬ Completed Task   
 ▬ Other Work Load  
◆ Milestone   
 ▬ In-progress Task   
 ▬ Task Work Load   
 ▬ Free Load

# Fedora 14 Documentation & Translation Tasks & Milestones

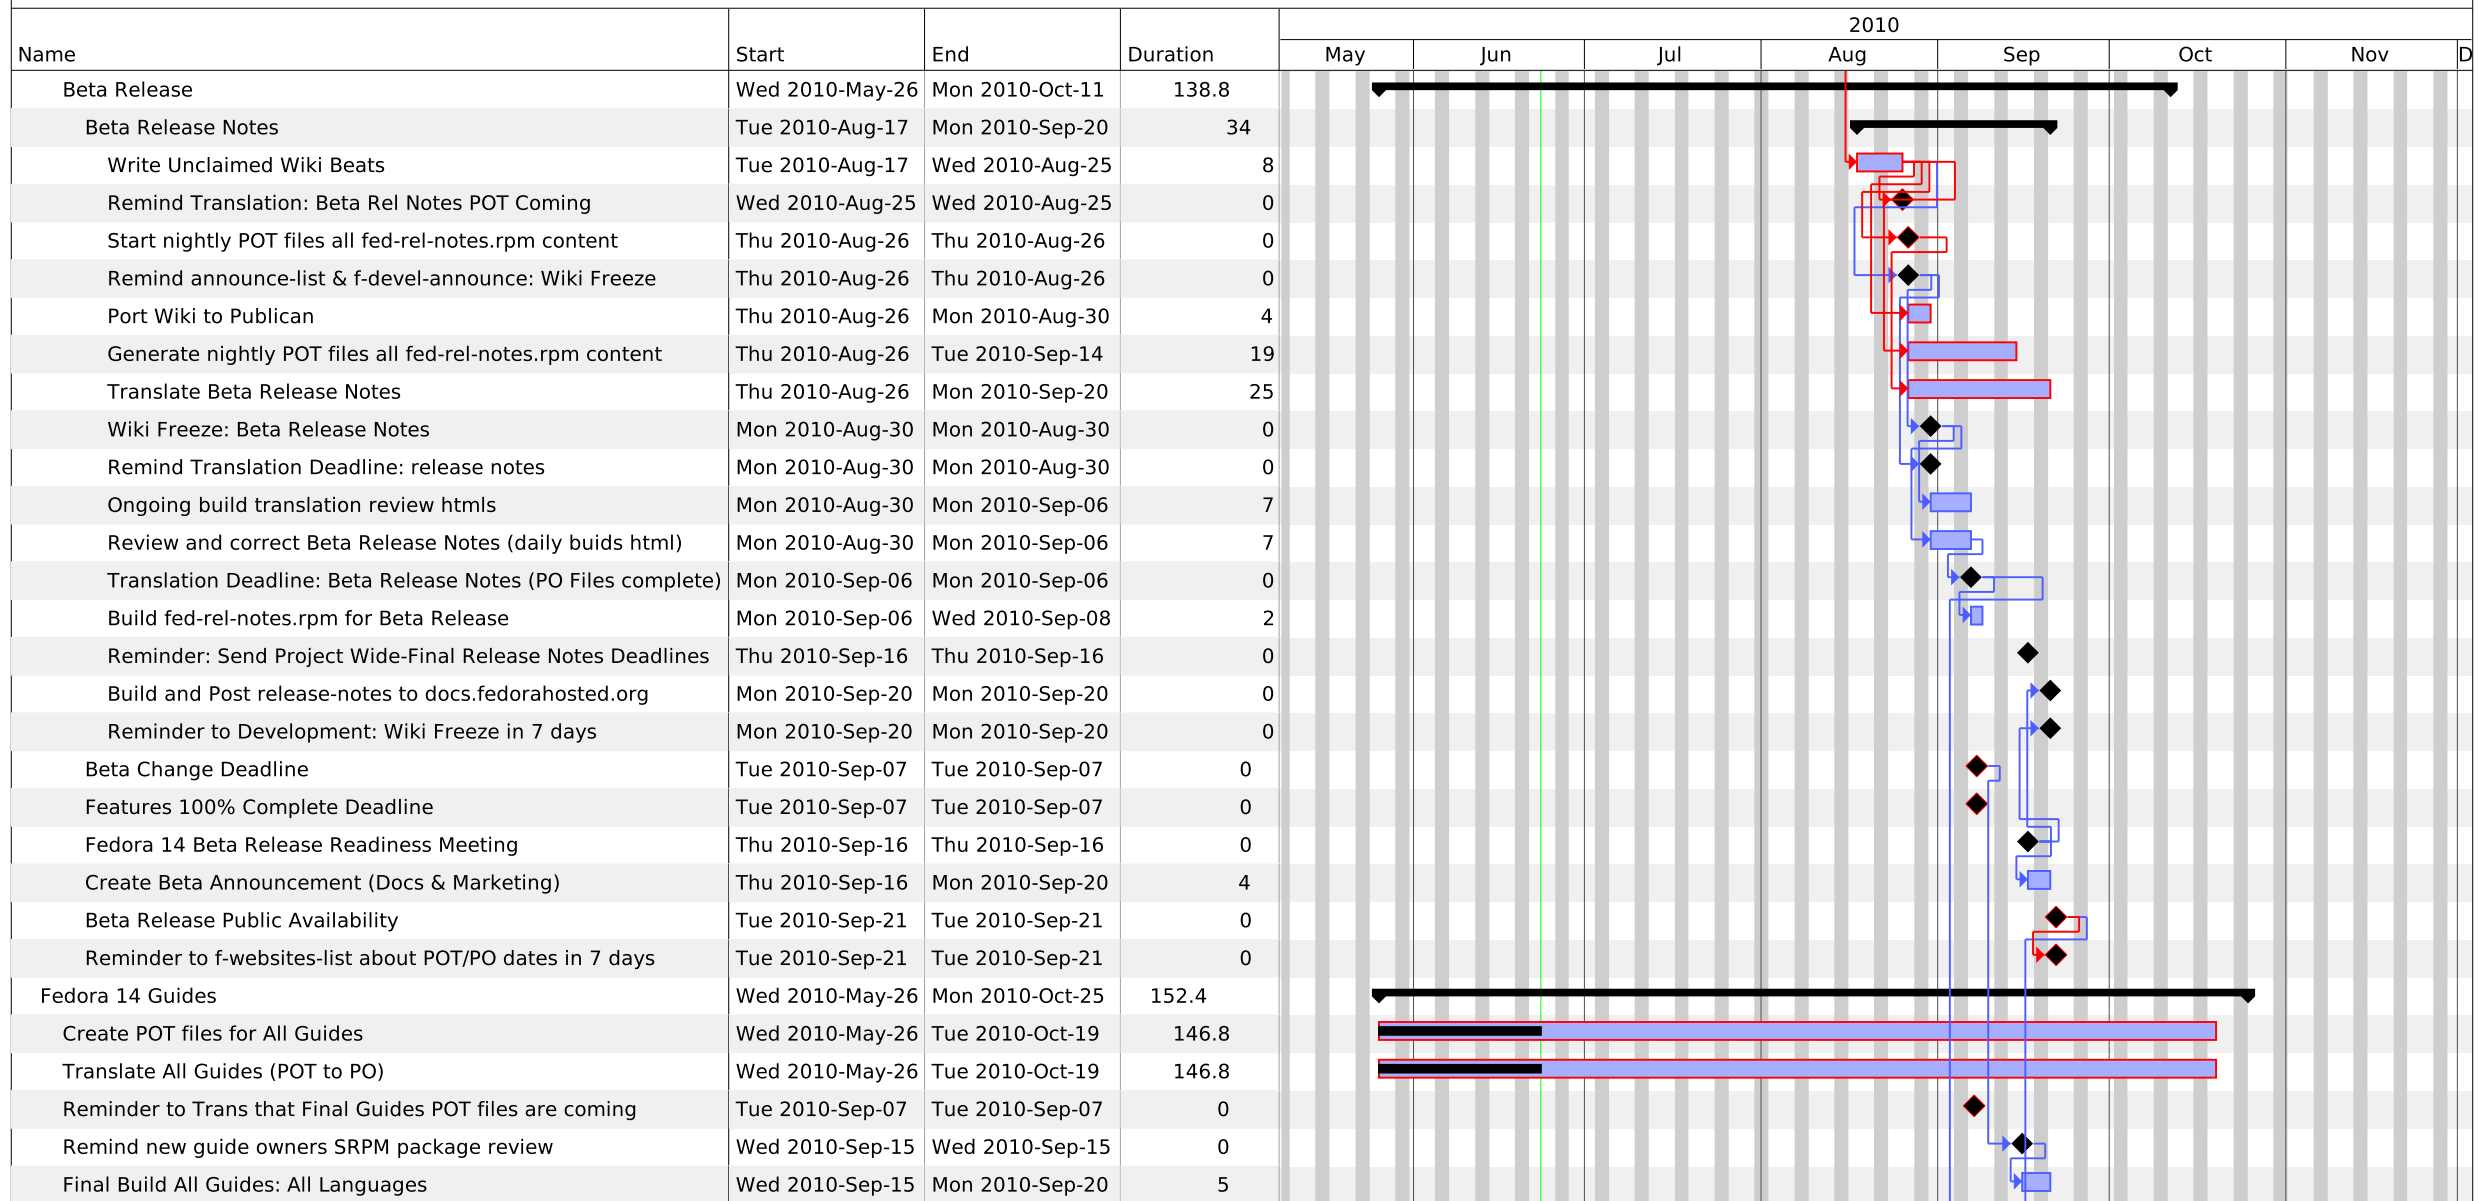

## Fedora 14 Documentation & Translation Tasks & Milestones

Name	Start	End	Duration	2010																		
				May	Jun	Jul	Aug	Sep	Oct	Nov	D											
Daily builds of Final guides for Translation	Mon 2010-Oct-11	Fri 2010-Oct-22	11																			
Review and correct Final Translated Guides (daily builds html)	Mon 2010-Oct-11	Fri 2010-Oct-22	11																			
Translation Deadline: All Final Guides	Mon 2010-Oct-25	Mon 2010-Oct-25	0																			
Publish all guides to docs.fp.o (html,html-single,pdf)	Mon 2010-Oct-25	Mon 2010-Oct-25	0																			
Launch Phase	Wed 2010-May-26	Mon 2010-Nov-15	173.8	▶																		
Release Candidate	Wed 2010-May-26	Mon 2010-Nov-01	159.8	▶																		
Zero Day Release Notes	Wed 2010-May-26	Mon 2010-Nov-01	159.8	▶																		
0-Day rel-notes update docs.fp.org	Mon 2010-Oct-18	Mon 2010-Oct-25	7.4																			
0-Day rel-notes build updated rpm	Mon 2010-Oct-18	Mon 2010-Oct-25	7.4																			
0-Day rel-notes generate POT	Mon 2010-Oct-18	Mon 2010-Oct-25	7.4																			
Translate rel-notes nightly POT builds	Mon 2010-Oct-18	Mon 2010-Oct-25	7.4																			
Translation Deadline: 0-Day (PO Files complete)	Mon 2010-Oct-25	Mon 2010-Oct-25	0																			
Add translated zero-day updates to docs.fp.org	Mon 2010-Oct-25	Mon 2010-Oct-25	0																			
Push updated rel-notes RPMs to Updates repo	Mon 2010-Nov-01	Mon 2010-Nov-01	0																			
Final Release Notes	Tue 2010-Sep-07	Wed 2010-Oct-13	36																			
Translate Final Release Notes (POT to PO)	Tue 2010-Sep-07	Mon 2010-Oct-11	34																			
Prepare GA Release Notes	Tue 2010-Sep-21	Tue 2010-Sep-21	0																			
String Freeze: GA Release Notes	Mon 2010-Sep-27	Mon 2010-Sep-27	0																			
Port diff wiki content to Publican	Mon 2010-Sep-27	Mon 2010-Oct-04	7																			
Remind Translation: RPM Freeze (no more POTs) in 5 days	Wed 2010-Sep-29	Wed 2010-Sep-29	0																			
Generate GA Release Notes POT files for Translation	Mon 2010-Oct-04	Mon 2010-Oct-04	0																			
Build GA release note htmls for Translation	Tue 2010-Oct-05	Mon 2010-Oct-11	6																			
Review and correct GA Release Notes (daily builds html)	Tue 2010-Oct-05	Mon 2010-Oct-11	6																			
Remind Translators of GA Release Notes Deadline in 4 days	Thu 2010-Oct-07	Thu 2010-Oct-07	0																			
Translation Deadline: GA rel-notes (PO Files complete)	Mon 2010-Oct-11	Mon 2010-Oct-11	0																			
Build fedora-release-notes.rpm	Mon 2010-Oct-11	Wed 2010-Oct-13	2																			
Translation Period for Website (POT to PO)	Wed 2010-Sep-29	Tue 2010-Oct-12	13																			
Create GA Announcement (Docs & Marketing)	Fri 2010-Oct-08	Mon 2010-Oct-18	10.4																			
Final Change Deadline	Mon 2010-Oct-11	Mon 2010-Oct-11	0																			
Compose 'Final' RC	Tue 2010-Oct-12	Thu 2010-Oct-14	2																			

▶ Container Task   
 ▭ Planned Task   
 ▬ Completed Task   
 ▭ Other Work Load  
◆ Milestone   
 ▭ In-progress Task   
 ▭ Task Work Load   
 ▭ Free Load

## Fedora 14 Documentation & Translation Tasks & Milestones

Name	Start	End	Duration	2010																		
				May	Jun	Jul	Aug	Sep	Oct	Nov	D											
Review and correct Website translations	Tue 2010-Oct-12	Mon 2010-Oct-18	6																			
Translation Deadline: Websites (POs done)	Mon 2010-Oct-18	Mon 2010-Oct-18	0																			
Translate GA Announcement	Mon 2010-Oct-18	Mon 2010-Oct-25	7																			
Fedora 14 Final Release Readiness Meeting	Tue 2010-Oct-19	Tue 2010-Oct-19	0																			
Fedora 14 Final Go/No-Go Meeting (17:00 EST)	Tue 2010-Oct-19	Tue 2010-Oct-19	0																			
Translation Deadline: GA Announcement	Mon 2010-Oct-25	Mon 2010-Oct-25	0																			
Final (GA) Release	Tue 2010-Oct-26	Tue 2010-Oct-26	0																			

- Container Task
  Planned Task
  Completed Task
  Other Work Load
- Milestone
  In-progress Task
  Task Work Load
  Free Load
